


Regional Internet Service Expansion (RISE) Project

The Power of Partnerships

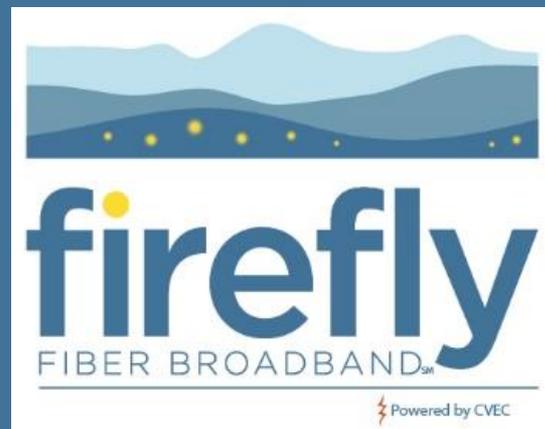


Goochland County Project Partners

Firefly Fiber BroadbandSM

Dominion Energy

Rappahannock Electric


Goochland County



Goochland Connection and Construction Status

- Areas in Service - Cartersville
- Passings –710 (includes 110 in Cartersville circuit)
- Active Accounts – 50 online plus 448 registered and waiting
 - 70% take rate for registration
- Miles of fiber – Approximately 91 miles (64 OH and 27 UG)
- Total investment - \$3.5 million
- Firefly field data gathering will begin soon for ReConnect and VATI
 - Residents will be notified by mail prior to our crews being in the area

Firefly RISE Project: Goochland County

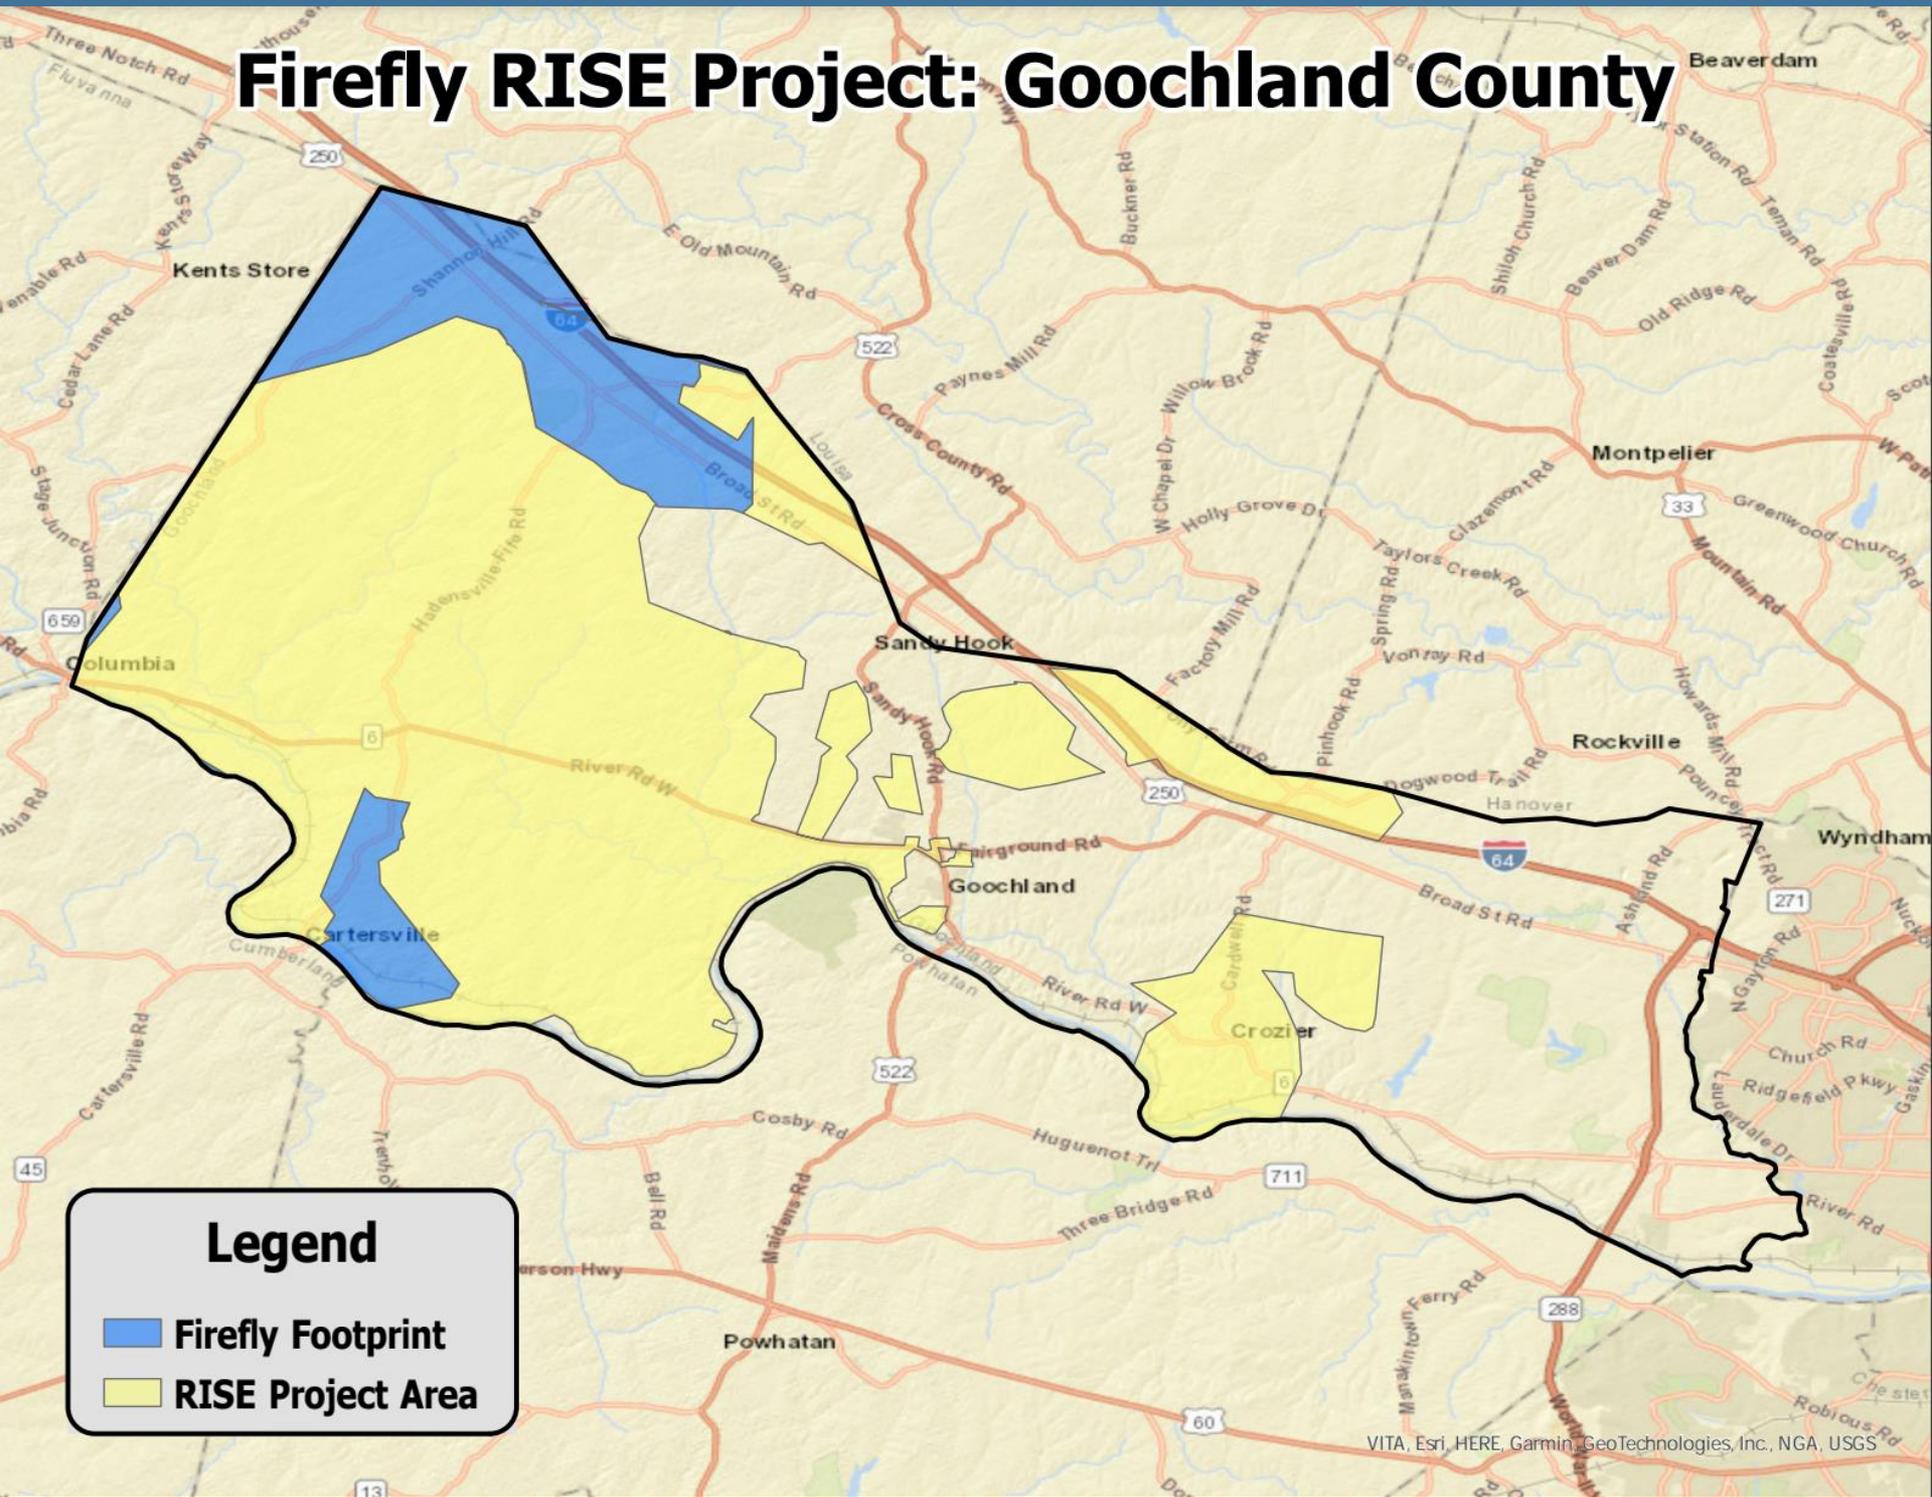

Final RISE Project Figures in Goochland

- VATI Project Total- \$27,709,235
- CAF Project Total- \$1,435,160
- Total RISE Project Total- \$29,144,395
 - ReConnect - \$6 million more
- VATI Award Total for County- \$3,977,794
- Approved County VATI Match Contribution- \$3,025,400
 - County also contributed \$200,000 to ReConnect
- Total passings within RISE and CVEC- 3,538
- Passings in ReConnect - 825
- Total Miles of Fiber - 320 miles in all projects
- VATI Award Total - \$79,027,930

Areas Under Construction or Announced to Start

1. Shannon Hill is under construction and splicing has started. Drop placement will start soon and connections will start by end of Spring 2022.
2. Mt. Hope – Rappahannock Electric Cooperative (REC) has started the data collection and make ready construction
 - Hadensville Farm Ln
 - Pony Farm Rd
3. Reconnect II – Environment review is pending state approval
4. Dominion Energy (DE) – middle mile routes are being reviewed and DE has started field verification and ride outs

Steps of Fiber Construction and Timeline

- Generally, assume six months from start of construction until first in home connections. Will continue to work until all who would like service are connected.
- Each area requires several steps before connections can be made:
 - Data collection (Firefly - NTS)
 - Design (Firefly - Conexon)
 - Make ready engineering
 - Make ready construction
 - Fiber construction (Firefly - S&N)
 - Splicing (Firefly - S&N)
 - Service extensions to homes (Firefly - S&N)
 - Final connection (Firefly)

Committed to Affordable Service

Residential Services

Firefly Light 100 Mbps	\$49.99
Firefly Flash 1 Gbps	\$79.99
Whole Home WiFi	\$5.99
Firefly Phone*	\$29.99

*Includes \$5 discount with
Flash or Light Services

The Firefly Difference

Whole Home WiFi: Support when you need it most

Lightning Fast: Up to 1 Gbps symmetrical upload and download speeds

Free WiFi Equipment: Get the most out of your speed with the latest technology

Fair Pricing: No hidden equipment costs or price increases after sign-up and no contract

Honest Service: No usage or data caps

Reliable Network: No slowdowns due to weather or too many users online



firefly
FIBER BROADBANDSM

⚡ Powered by CVEC



firefly
FIBER BROADBANDSM

Questions? Visit our online resources

Have questions on whether your location is in our RISE Project?

Visit: <https://www.fireflyva.com/rise/>



[About Us](#) [Business](#) [Residential](#) [News & Press](#) [Partners](#) [Help](#)



[Login/Pay Bill](#)

[Check Availability](#)

Firefly is spreading its wings.

The Regional Internet Service Expansion (RISE) Project will bring reliable, affordable fiber internet to more Central Virginians.

[View Construction Updates](#)

[View All Partners](#)



[Regional Internet Service Expansion \(RISE\) Project](#)

Update: December 2021

The RISE Project is an initiative by Firefly Fiber BroadbandSM, a wholly-owned subsidiary of Central Virginia Electric Cooperative (CVEC), to provide internet

firefly
FIBER BROADBANDSM
